RENOVATIONS TO FEDERAL OFFICE COMPLEX
Baseline vs. Updated Project Schedule Comparison

Effect of Logic Revisions to Millwork Activities

Baseline Project Schedule - BGBB

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	T F
Valley City					
Phase 1					
Byrne Building					
A09800B3W	Millwork Engineering (Byrne 3W)	24	17DEC96	27JAN97	0
A09805B3W	Inst. Millwrk Mock-up & Samples (Byrne 3W)	4	28JAN97	03FEB97	8
A09809B3W	Fab Mlwk - Diamonds/Faces/Shelving (Byrne 3W)	16	18FEB97	17MAR97	0
A09820B3W	Fab Mlwk - Wall Panels/Trim/Cabinets (Byrne 3W)	22	18MAR97	23APR97	0
A09821B3W	Fab Mlwk - Counters & Benches (Byrne 3W)	38	08APR97	11JUN97	0
A09900B3W6	4Ins. CR.6 Wall Pnls/Trim/Dr Frms (Byrne 3W)	4	06MAY97	12MAY97	2
A09900B3W7	Ins. CR.7 Wall Pnls/Trim/Dr Frms (Byrne 3W)	4	13MAY97	19MAY97	2
A09901B3W4	Ins. CR.4 Wall Pnls/Trim/Dr Frms (Byrne 3W)	4	15MAY97	21MAY97	0
A09901B3W5	Ins. CR.5 Wall Pnls/Trim/Dr Frms (Byrne 3W)	4	22MAY97	28MAY97	0
A09902B3W6	Ins. CR.6 Jdg/Jry/Clrk Benchs (Byrne 3W)	4	05JUN97	11JUN97	0
A09902B3W7	Ins. CR.7 Jdg/Jry/Clrk Benchs (Byrne 3W)	4	12JUN97	18JUN97	0
A09903B3W4	Ins. CR.4 Jdg/Jry/Clrk Benchs (Byrne 3W)	4	19JUN97	25JUN97	0
A09903B3W5	Ins. CR.5 Jdg/Jry/Clrk Benchs (Byrne 3W)	4	26JUN97	02JUL97	0
A09904B3W5	Ins. CR.7&6 Platforms (Byrne 3W)	3	03JUL97	08JUL97	0
A09905B3W	Ins. CR.4&5 Platforms (Byrne 3W)	3	09JUL97	14JUL97	0
A09907B3W	Install Misc Counters & Shelving (Byrne 3W)	4	29MAY97	04JUN97	0
A09908B3W	Ins. CR.7&6 Gallery Seating (Byrne 3W)	2	30JUL97	31JUL97	1
A09909B3W	Ins. CR.4&5 Gallery Seating (Byrne 3W)	2	05AUG97	06AUG97	0

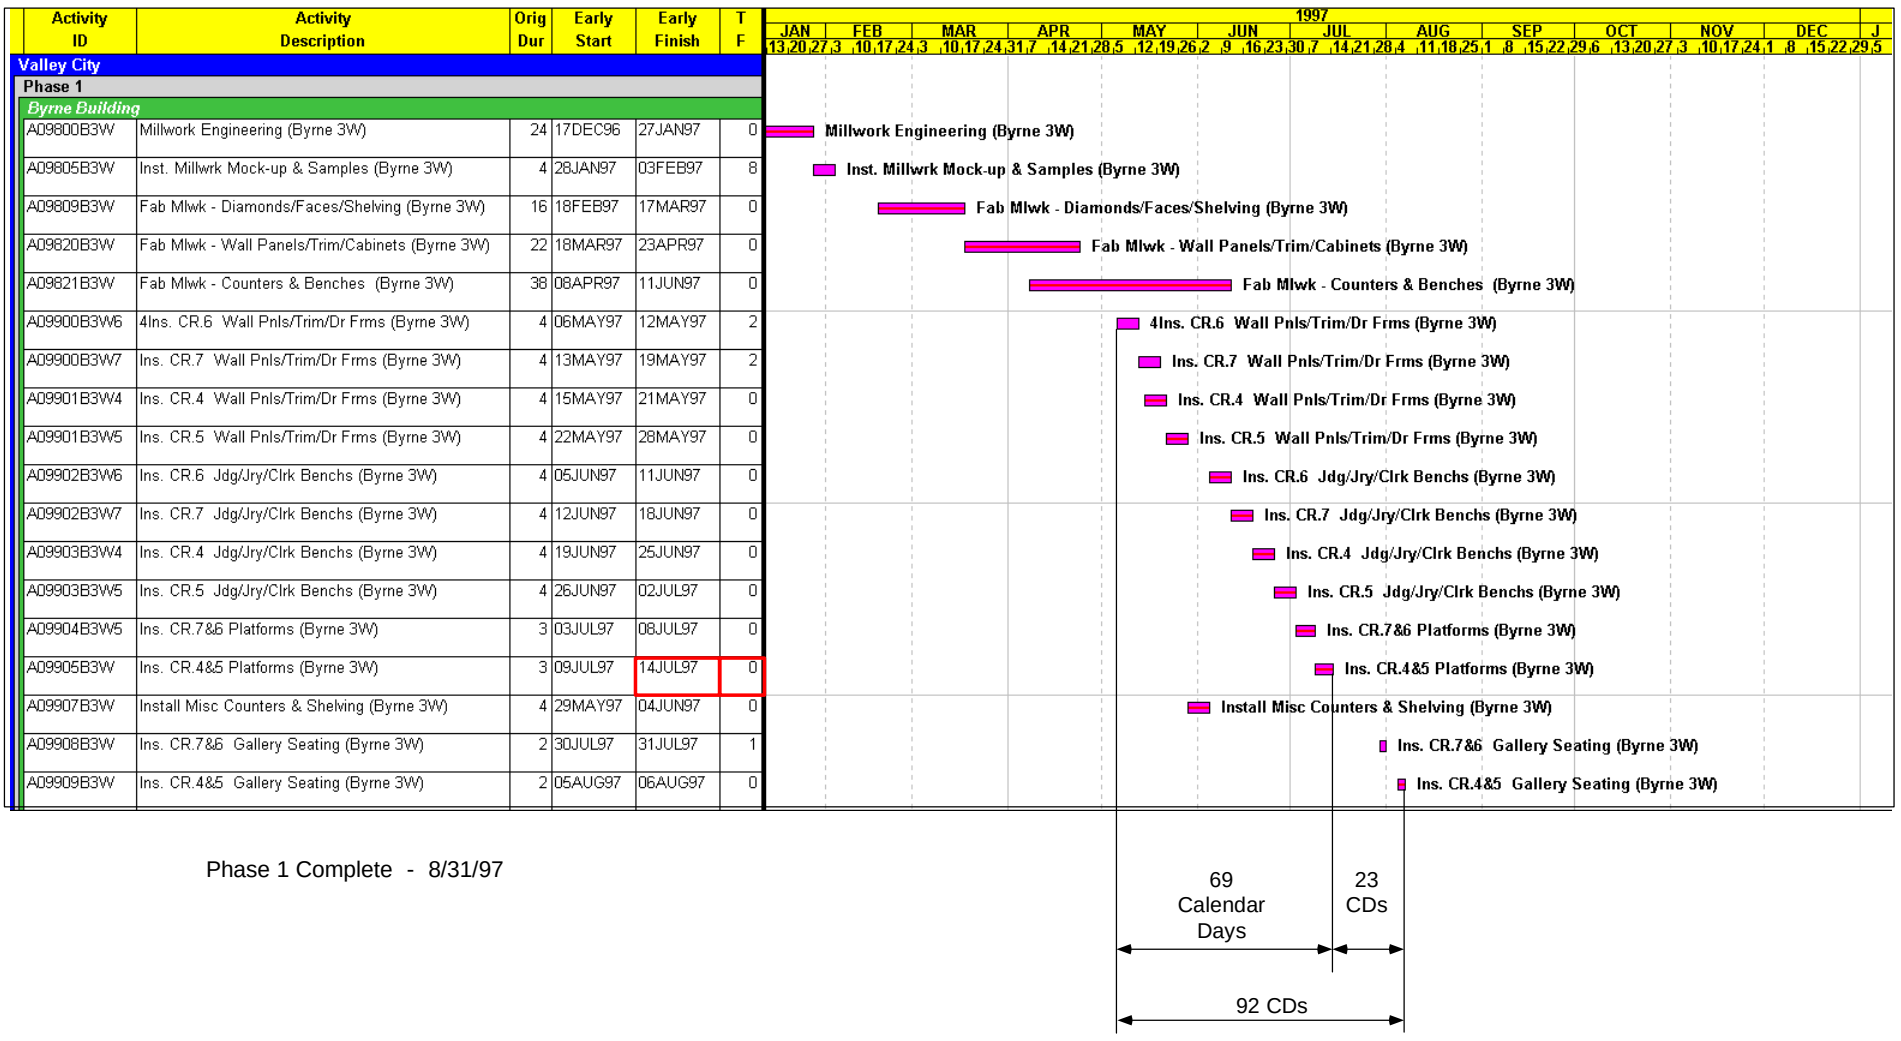

Phase 1 Complete - 8/31/97

Updated Project Schedule - BG1B

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	T F
Valley City					
Phase 1					
Byrne Building					
A09800B3W	Millwork Engineering (Byrne 3W)	24	20JAN97A	20FEB97A	
A09805B3W	Inst. Millwrk Mock-up & Samples (Byrne 3W)	4	05FEB97A	05MAY97A	
A09809B3W	Fab Mlwk - Diamonds/Faces/Shelving (Byrne 3W)	16	15APR97A	26MAY97	-12
A09820B3W	Fab Mlwk - Wall Panels/Trim/Cabinets (Byrne 3W)	22	21APR97A	09JUN97	-12
A09821B3W	Fab Mlwk - Counters & Benches (Byrne 3W)	38	21APR97A	18JUN97	0
A09900B3W6	Ins. CR.6 Wall Pnls/Trim/Dr Frms (Byrne 3W)	4	09JUN97	12JUN97	-15
A09900B3W7	Ins. CR.7 Wall Pnls/Trim/Dr Frms (Byrne 3W)	4	16JUN97	19JUN97	-15
A09901B3W4	Ins. CR.4 Wall Pnls/Trim/Dr Frms (Byrne 3W)	4	16JUN97	19JUN97	-15
A09901B3W5	Ins. CR.5 Wall Pnls/Trim/Dr Frms (Byrne 3W)	4	23JUN97	26JUN97	-15
A09902B3W6	Ins. CR.6 Jdg/Jry/Clrk Benchs (Byrne 3W)	4	30JUN97	03JUL97	-5
A09902B3W7	Ins. CR.7 Jdg/Jry/Clrk Benchs (Byrne 3W)	4	07JUL97	10JUL97	-5
A09903B3W4	Ins. CR.4 Jdg/Jry/Clrk Benchs (Byrne 3W)	4	30JUN97	03JUL97	-5
A09903B3W5	Ins. CR.5 Jdg/Jry/Clrk Benchs (Byrne 3W)	4	07JUL97	10JUL97	-5
A09904B3W5	Ins. CR.7&6 Platforms (Byrne 3W)	3	14JUL97	16JUL97	-5
A09905B3W	Ins. CR.4&5 Platforms (Byrne 3W)	3	17JUL97	22JUL97	-5
A09907B3W	Install Misc Counters & Shelving (Byrne 3W)	4	23JUN97	26JUN97	-5
A09908B3W	Ins. CR.7&6 Gallery Seating (Byrne 3W)	2	07AUG97	11AUG97	-4
A09909B3W	Ins. CR.4&5 Gallery Seating (Byrne 3W)	2	21AUG97	25AUG97	-10

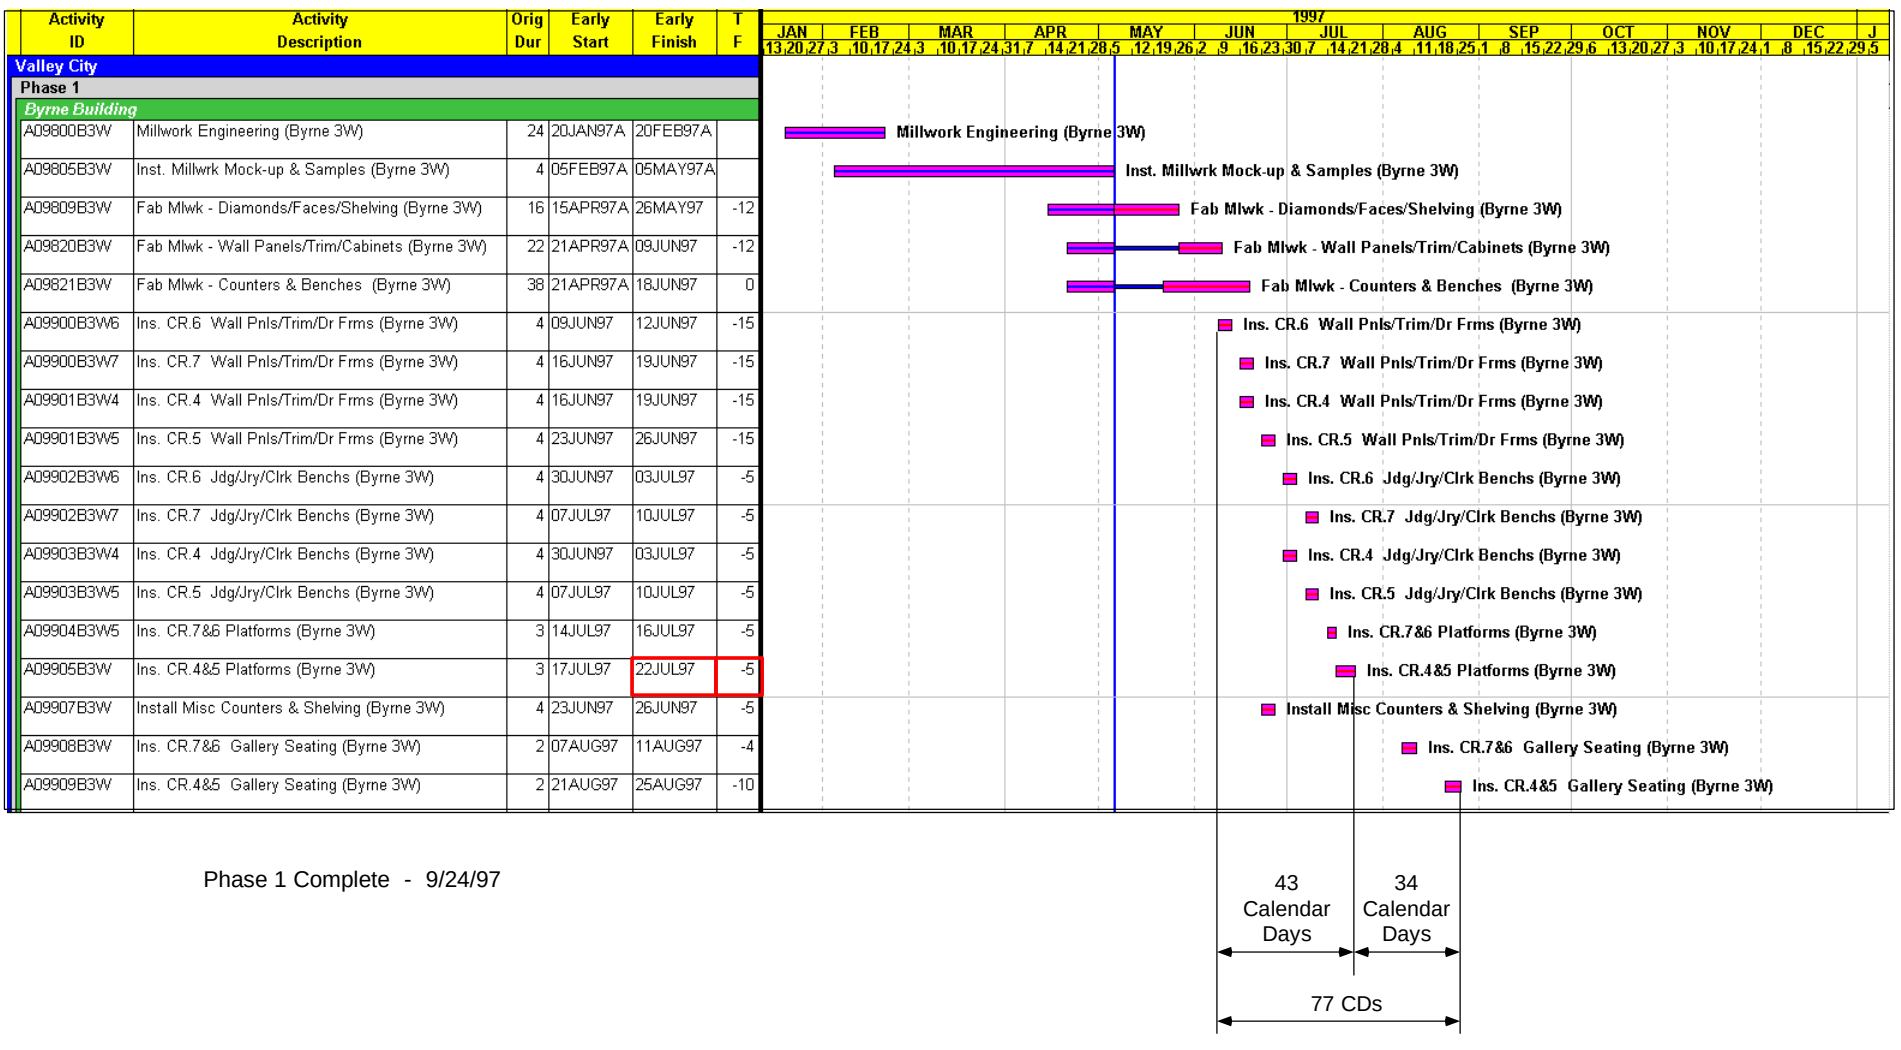

Phase 1 Complete - 9/24/97

15 Net Calendar Day Recovery Through Millwork Activities
